








ID		Task Name	Duration	Start	Finish	Jan 2, '05							Jan 9, '05								
						T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F
33		Economic Review Completed	1 day?	Tue 1/25/05	Wed 1/26/05																
34		Additional Econ Info Requested	1 day?	Wed 1/26/05	Thu 1/27/05																
35		Additional Econ Info Provided	1 day?	Thu 1/27/05	Fri 1/28/05																
36		Compliance Issues Identified	1 day?	Wed 1/26/05	Thu 1/27/05																
37		Compliance Decision Communicated	0 days	Thu 1/27/05	Thu 1/27/05																
38		Communicate Progress	1 day?	Thu 1/27/05	Fri 1/28/05																
39		Request "other" Additional Info Needs	0 days	Fri 1/28/05	Fri 1/28/05																
40		Review Department Analysis	1 day?	Fri 1/28/05	Mon 1/31/05																
41		Project Update w/ Supervisor	1 day?	Mon 1/31/05	Tue 2/1/05																
42		EPA Consulted	1 day?	Tue 2/1/05	Wed 2/2/05																
43		Conclusions / Results Completed	1 day?	Wed 2/2/05	Thu 2/3/05																
44		Draft Permits Completed	1 day?	Thu 2/3/05	Fri 2/4/05																
45		Modeling Analysis	8 days?	Fri 1/14/05	Thu 1/27/05																
46		Modeling Submitted	0 days	Fri 1/14/05	Fri 1/14/05																
47		Preliminary Modeling Review Completed	1 day?	Tue 1/18/05	Wed 1/19/05																
48		Additional Information Needed	1 day?	Wed 1/19/05	Thu 1/20/05																
49		Modeling Review	1 day?	Thu 1/20/05	Fri 1/21/05																
50		Visibility Review Completed	1 day?	Fri 1/21/05	Mon 1/24/05																
51		Soils & Vegetation Review Completed	1 day?	Tue 1/25/05	Wed 1/26/05																
52		EPA Consultation	1 day?	Wed 1/26/05	Thu 1/27/05																
53		Additional Information Request	1 day?	Wed 1/26/05	Thu 1/27/05																
54		Final Modeling Approved	0 days	Thu 1/27/05	Thu 1/27/05																
55		Permit Finalization	16 days?	Fri 2/4/05	Tue 3/1/05																
56		Draft Permit Review Completed	1 day?	Fri 2/4/05	Mon 2/7/05																
57		Provide Draft Permit to Facility	1 day?	Mon 2/7/05	Tue 2/8/05																
58		Provide Draft Permit to EPA	1 day?	Mon 2/7/05	Tue 2/8/05																
59		Sr. Engineer Review Completed	1 day?	Mon 2/7/05	Tue 2/8/05																
60		Facility Review of Draft Permits Completed	1 day?	Tue 2/8/05	Wed 2/9/05																
61		Prepare for Public Hearing	1 day?	Wed 2/9/05	Thu 2/10/05																
62		Hold Public Hearing	1 day?	Thu 2/10/05	Fri 2/11/05																
63		Public Comment Preparation Completed	1 day?	Fri 2/11/05	Mon 2/14/05																
64		Public Comment Period Held	1 day?	Mon 2/14/05	Tue 2/15/05																

Project: PSD Kaizen
Date: Thu 10/21/04

Task 
Split 
Progress 


Milestone 
Summary 
Project Summary 

External Tasks 
External Milestone 
Deadline 


ID		Task Name	Duration	Start	Finish				Jan 2, '05							Jan 9, '05						
						T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	
65		Public Comments Reviewed	1 day?	Wed 2/16/05	Thu 2/17/05																	
66		Response to Public Comments Completed	1 day?	Thu 2/17/05	Fri 2/18/05																	
67		Comment Responses Reviewed by Supervisor	1 day?	Fri 2/18/05	Mon 2/21/05																	
68		Draft Final Permits Completed	1 day?	Mon 2/21/05	Tue 2/22/05																	
69		Draft Final Permit Facility Review	1 day?	Tue 2/22/05	Wed 2/23/05																	
70		Final Permits Issues	1 day?	Wed 2/23/05	Thu 2/24/05																	
71		Info Entered into clearinghouse	1 day?	Thu 2/24/05	Fri 2/25/05																	
72		Project Logged Out	1 day?	Fri 2/25/05	Mon 2/28/05																	
73		Final Product Available	1 day?	Mon 2/28/05	Tue 3/1/05																	

Project: PSD Kaizen
Date: Thu 10/21/04


Task




Milestone




External Tasks




Split




Summary




External Milestone




Progress




Project Summary



Deadline



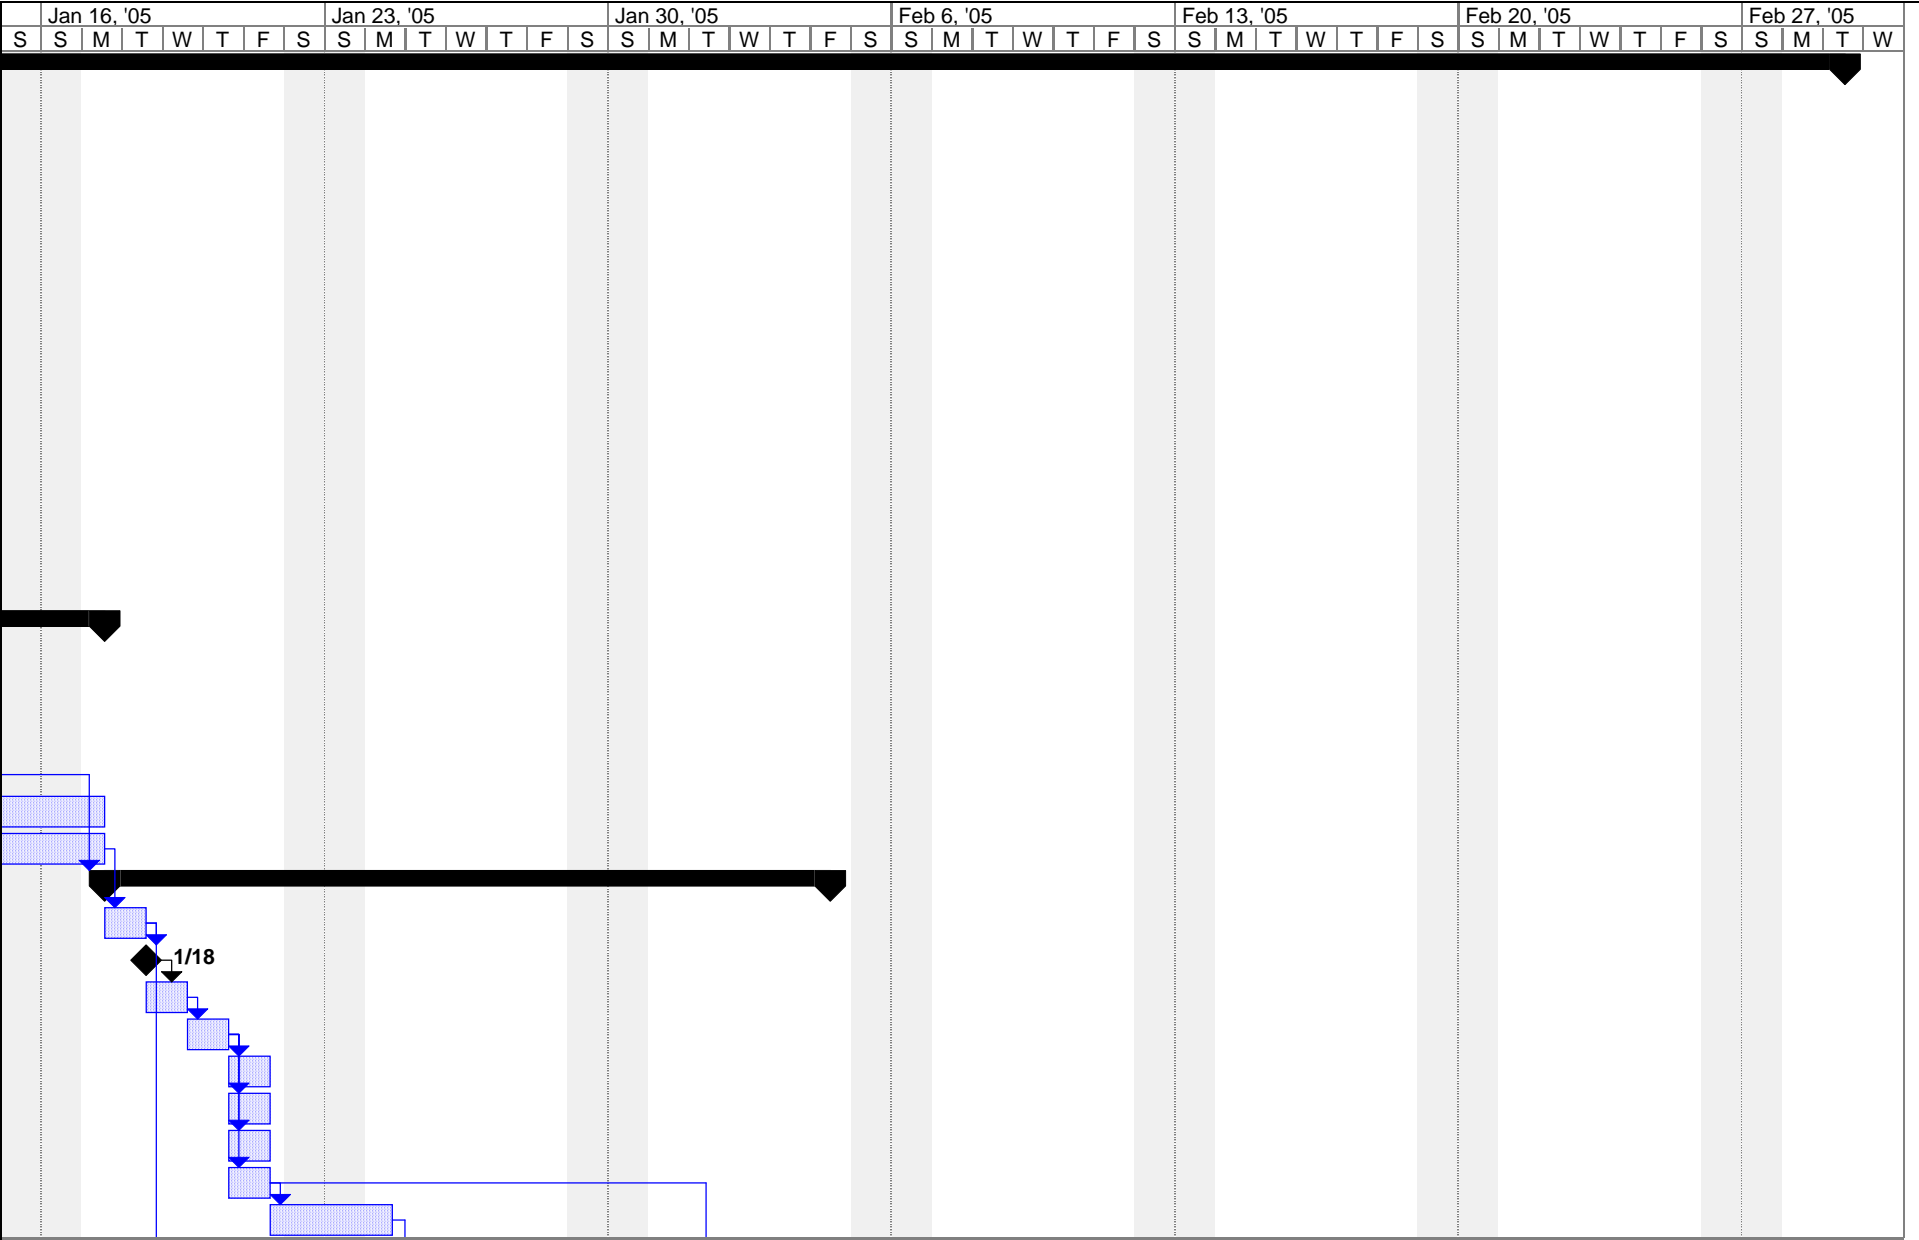

Project: PSD Kaizen
Date: Thu 10/21/04

Task

Split

Progress

Milestone


Summary

Project Summary

External Tasks

External Milestone

Deadline

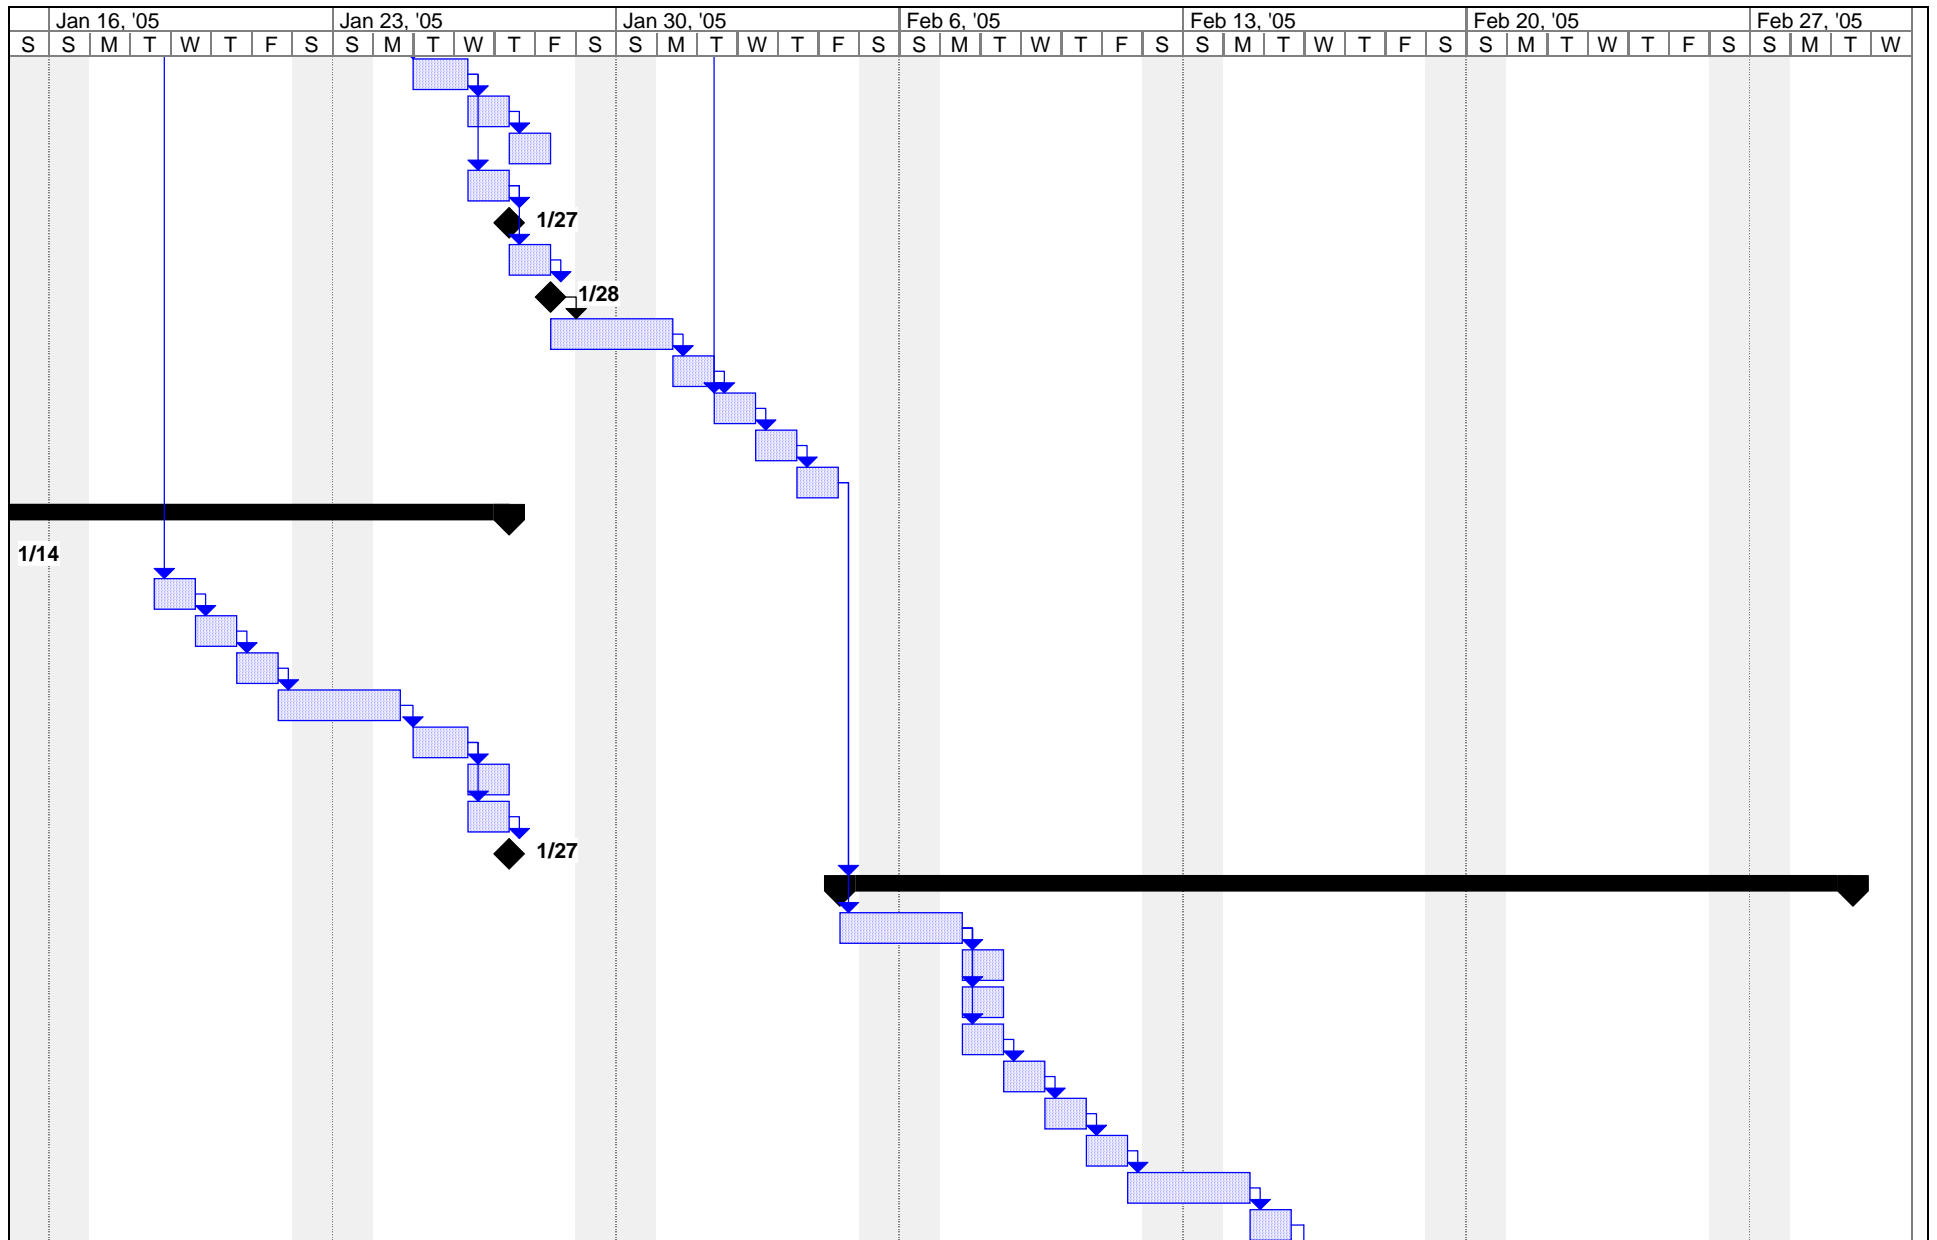

Project: PSD Kaizen
Date: Thu 10/21/04

Task

Split

Progress

Milestone

Summary

Project Summary

External Tasks

External Milestone

Deadline

